BRAVO environmental	**Date:** 11/10/2014 **Project:** Carillon Point Vault Cleaning
	Comments: All signs should conform to MUTCD specs Task: Clean Storm Water Control Structure Duration: 8 Hours Work Hours: 8AM - 5PM Work will be performed along Lake Washington Blvd Lanes moved to the east and divided by cones Minimum lane widths of 11 feet will be maintained

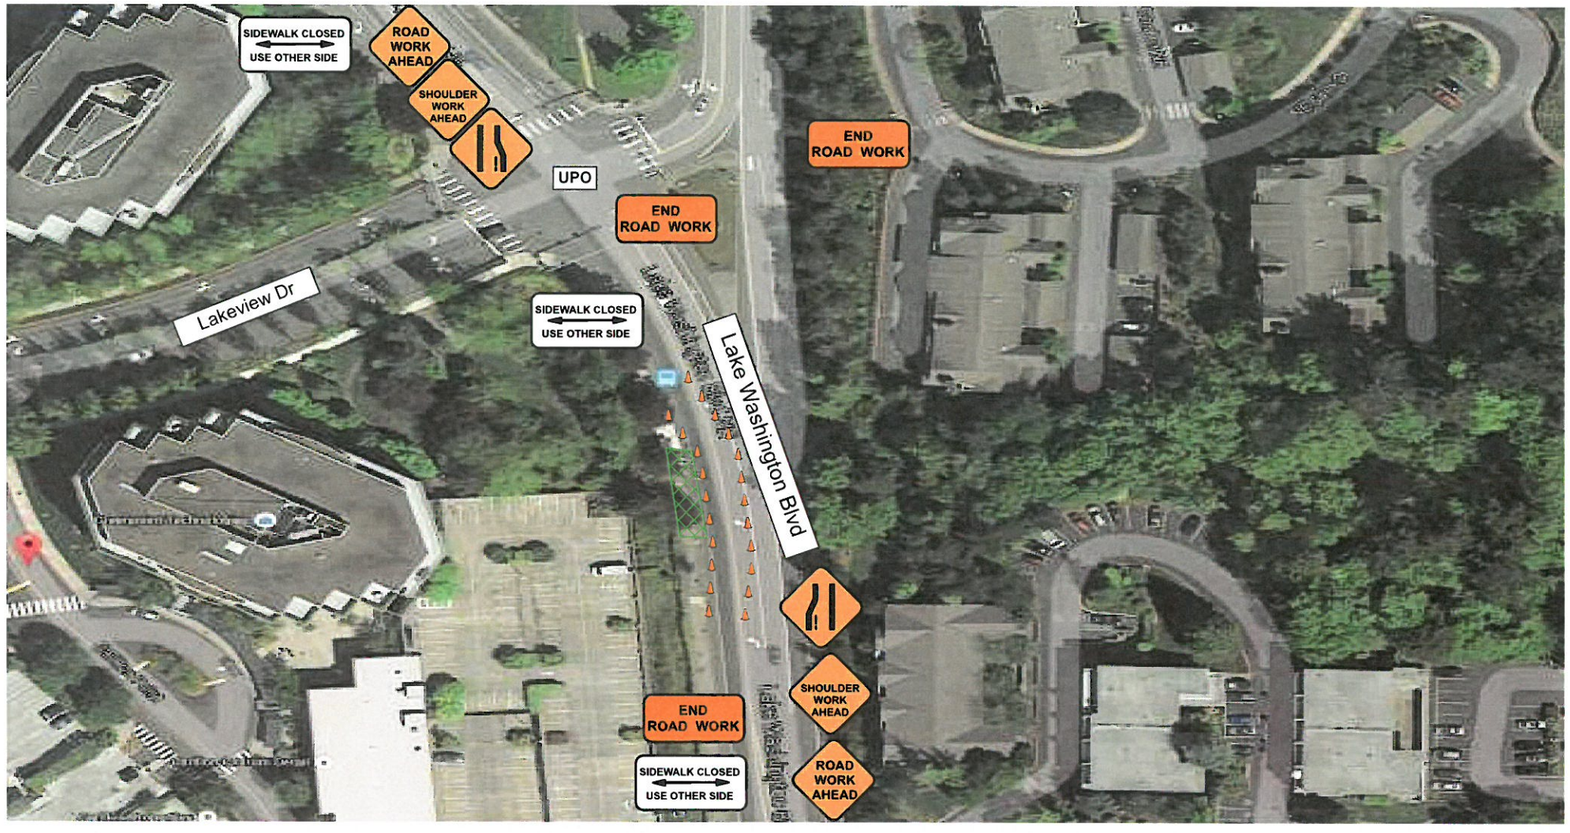

Manifest

22 x Cone

2 x road work ahead W20-1

2 x road narrows W4-2

3 x R9-10 R9-10

2 x Shoulder work W21-5c

3 x KG20-2 End of road work KG20-2

Legend

Work Area

Cone

Table 2C-4. Guidelines for Advance Placement of Warning Signs

Posted or 85th-Percentile Speed	Advance Placement Distance[1]								
	Condition A: Speed reduction and lane changing in heavy traffic[2]	Condition B: Deceleration to the listed advisory speed (mph) for the condition							
		0[3]	10[4]	20[4]	30[4]	40[4]	50[4]	60[4]	70[4]
20 mph	225 ft	100 ft[5]	N/A[5]	—	—	—	—	—	—
25 mph	325 ft	100 ft[5]	N/A[5]	N/A[5]	—	—	—	—	—
30 mph	460 ft	100 ft[5]	N/A[5]	N/A[5]	—	—	—	—	—
35 mph	565 ft	100 ft[5]	N/A[5]	N/A[5]	N/A[5]	—	—	—	—
40 mph	670 ft	125 ft	100 ft[5]	100 ft[5]	N/A[5]	—	—	—	—
45 mph	775 ft	175 ft	125 ft	100 ft[5]	100 ft[5]	N/A[5]	—	—	—
50 mph	885 ft	250 ft	200 ft	175 ft	125 ft	100 ft[5]	—	—	—
55 mph	990 ft	325 ft	275 ft	225 ft	200 ft	125 ft	N/A[5]	—	—
60 mph	1,100 ft	400 ft	350 ft	325 ft	275 ft	200 ft	100 ft[5]	—	—
65 mph	1,200 ft	475 ft	450 ft	400 ft	350 ft	275 ft	200 ft	100 ft[5]	—
70 mph	1,250 ft	550 ft	525 ft	500 ft	450 ft	375 ft	275 ft	150 ft	—
75 mph	1,350 ft	650 ft	625 ft	600 ft	550 ft	475 ft	375 ft	250 ft	100 ft[5]
